



Decommissioning Achievements	Year
All HEU (Cat 1 material) relocated off-site	2001
228 PCM Sea Dump Drums relocated off-site	2002
Phase 1 Delicensing achieved (A4 / B4)	2002
All 1660 Plutonium Contaminated Material (PCM) cans relocated off-site	2003
Complete packaging and storage of ILW arisings from A59 decommissioning	2003
First 100 tonnes of painted steelwork decontaminated using Winfrith Abrasive Cleaning Machine (WACM)	2004
Completed the relocation of LEU (Cat III material)	2004
Dragon Fuel Cans (Cat II material) relocated off-site	2004
East End of Site sold to English Partnerships	2004
SNP Transfer Operations	2005
SGHWR Front End Engineering	2006
148 Drums of asbestos were compacted to complete the asbestos supercompaction campaign	2006
SGHWR Main Cooling Water Pump Pit as part of Turbine Hall completed	2006
WETP Active Sludge successfully pumped around EAST	2006
SGHWR 59 Ton inner ring on the rotating shields was removed	2006
Sodium Coupon disposal completed	2006
Facilities Decommissioned	
Zenith Reactor	1975
Juno Reactor / Nero Reactor	1984
Hector Reactor	1990
B41 & B47 Laboratories	1998
Fuel Fabrication Buildings	1999
Dimple Reactor	2000
Nestor Reactor	2000
A40 Laboratories	2000
SGHWR Stack	2004
ALES Eastern part of the Active Liquid Effluent System	2004
B3 Complex	2005
ZEBRA Reactor	2005
B2 Complex	2006
Active Handling Building (A59)	2006
ZEBRA Complex	2009

Milestone Summary Schedule (Logic Linked)

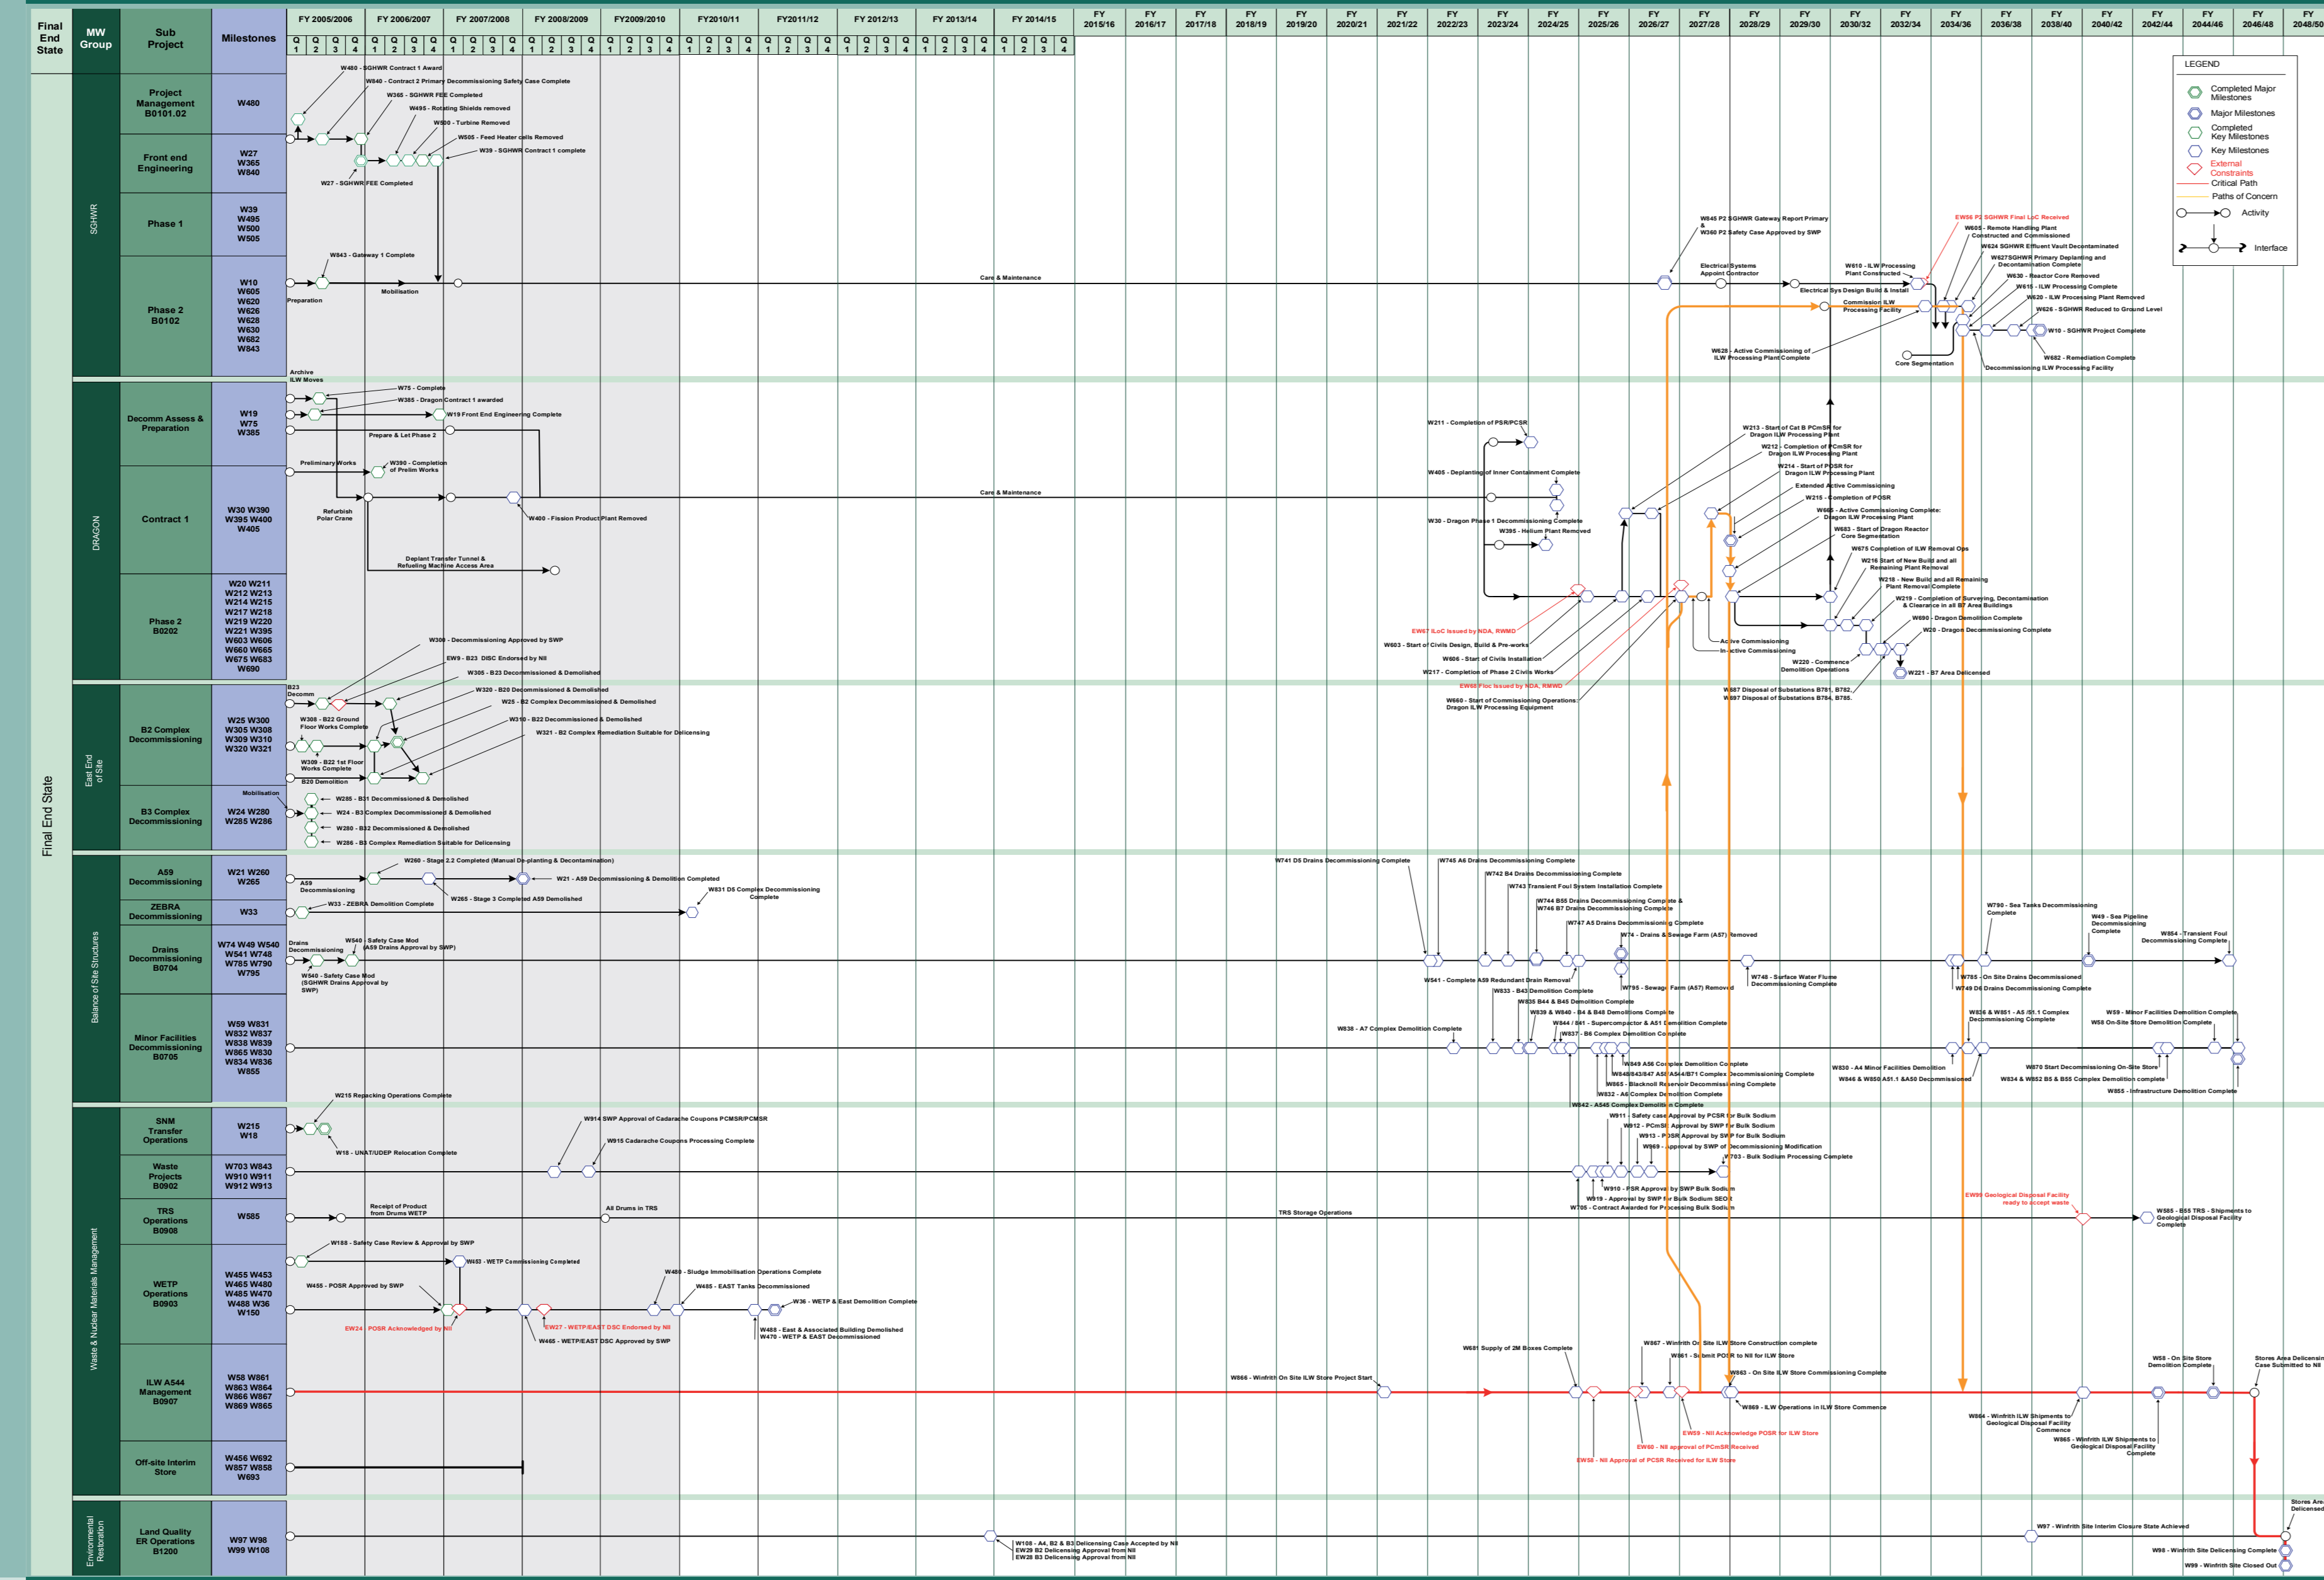


Milestone Sequencing Chart

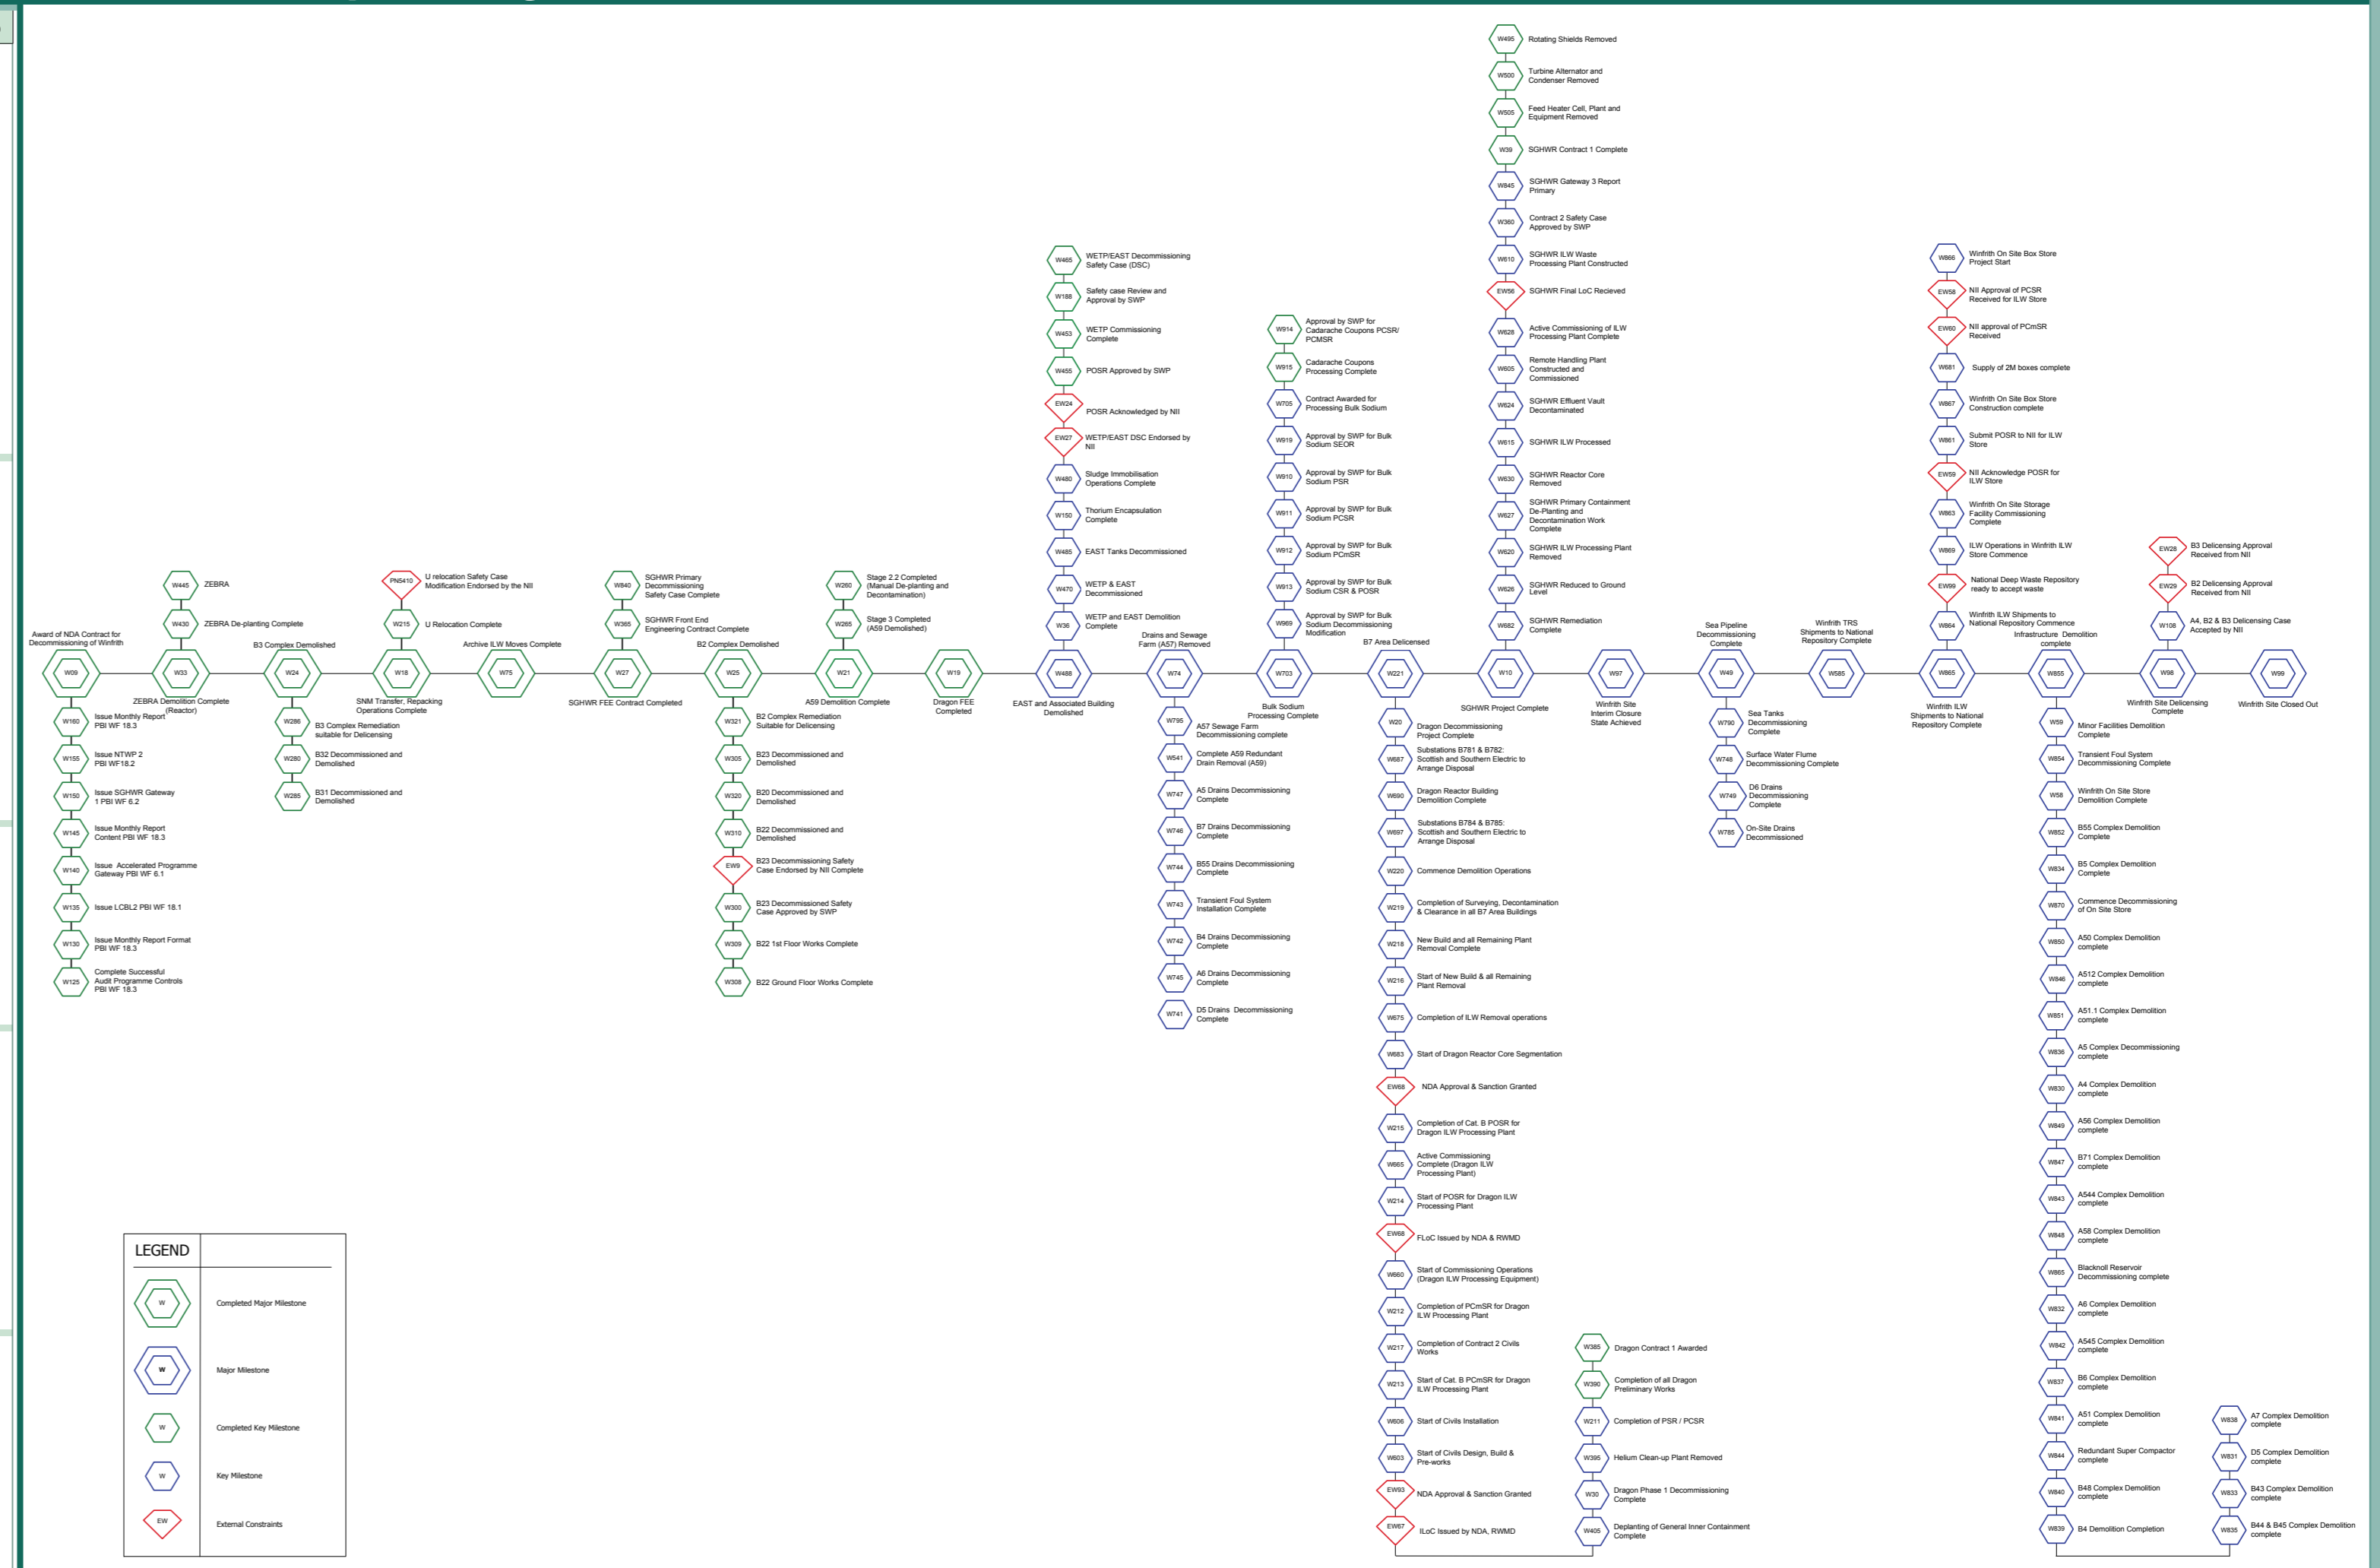

Decommissioning Targets	Year
A4, B2 & B3 Delicensing Case Accepted by NII	2010
WETP and EAST Demolition Complete	2010
A7 Complex Demolition complete	2022
D5 Complex Demolition complete	2023
B6 Complex Demolition complete	2024
Drains & Sewage Farm (A57) Removed	2026
Winfrith On-site Storage Facility Commissioning Complete	2028
Bulk Sodium Processing Complete	2028
Blacknoll Reservoir Decommissioning complete	2025
Dragon Decommissioning Project Complete	2032
Thorium Encapsulation Complete	2034
A4 Complex Decommissioning Complete	2034
A5 Complex Decommissioning Complete	2035
Sea Tanks Decommissioning Complete	2036
SGHWR Project Complete	2038
Winfrith Site Interim Closure State Achieved	2038
Sea Pipeline Decommissioning Complete	2040
Winfrith TRS Shipments to National Repository Complete	2043
Winfrith On-site Store Demolition Complete	2045
Minor Facilities Demolition Complete	2046
Winfrith Site Delicensing Complete	2048
Winfrith Site Closed Out	2048

Prioritisation Diagram

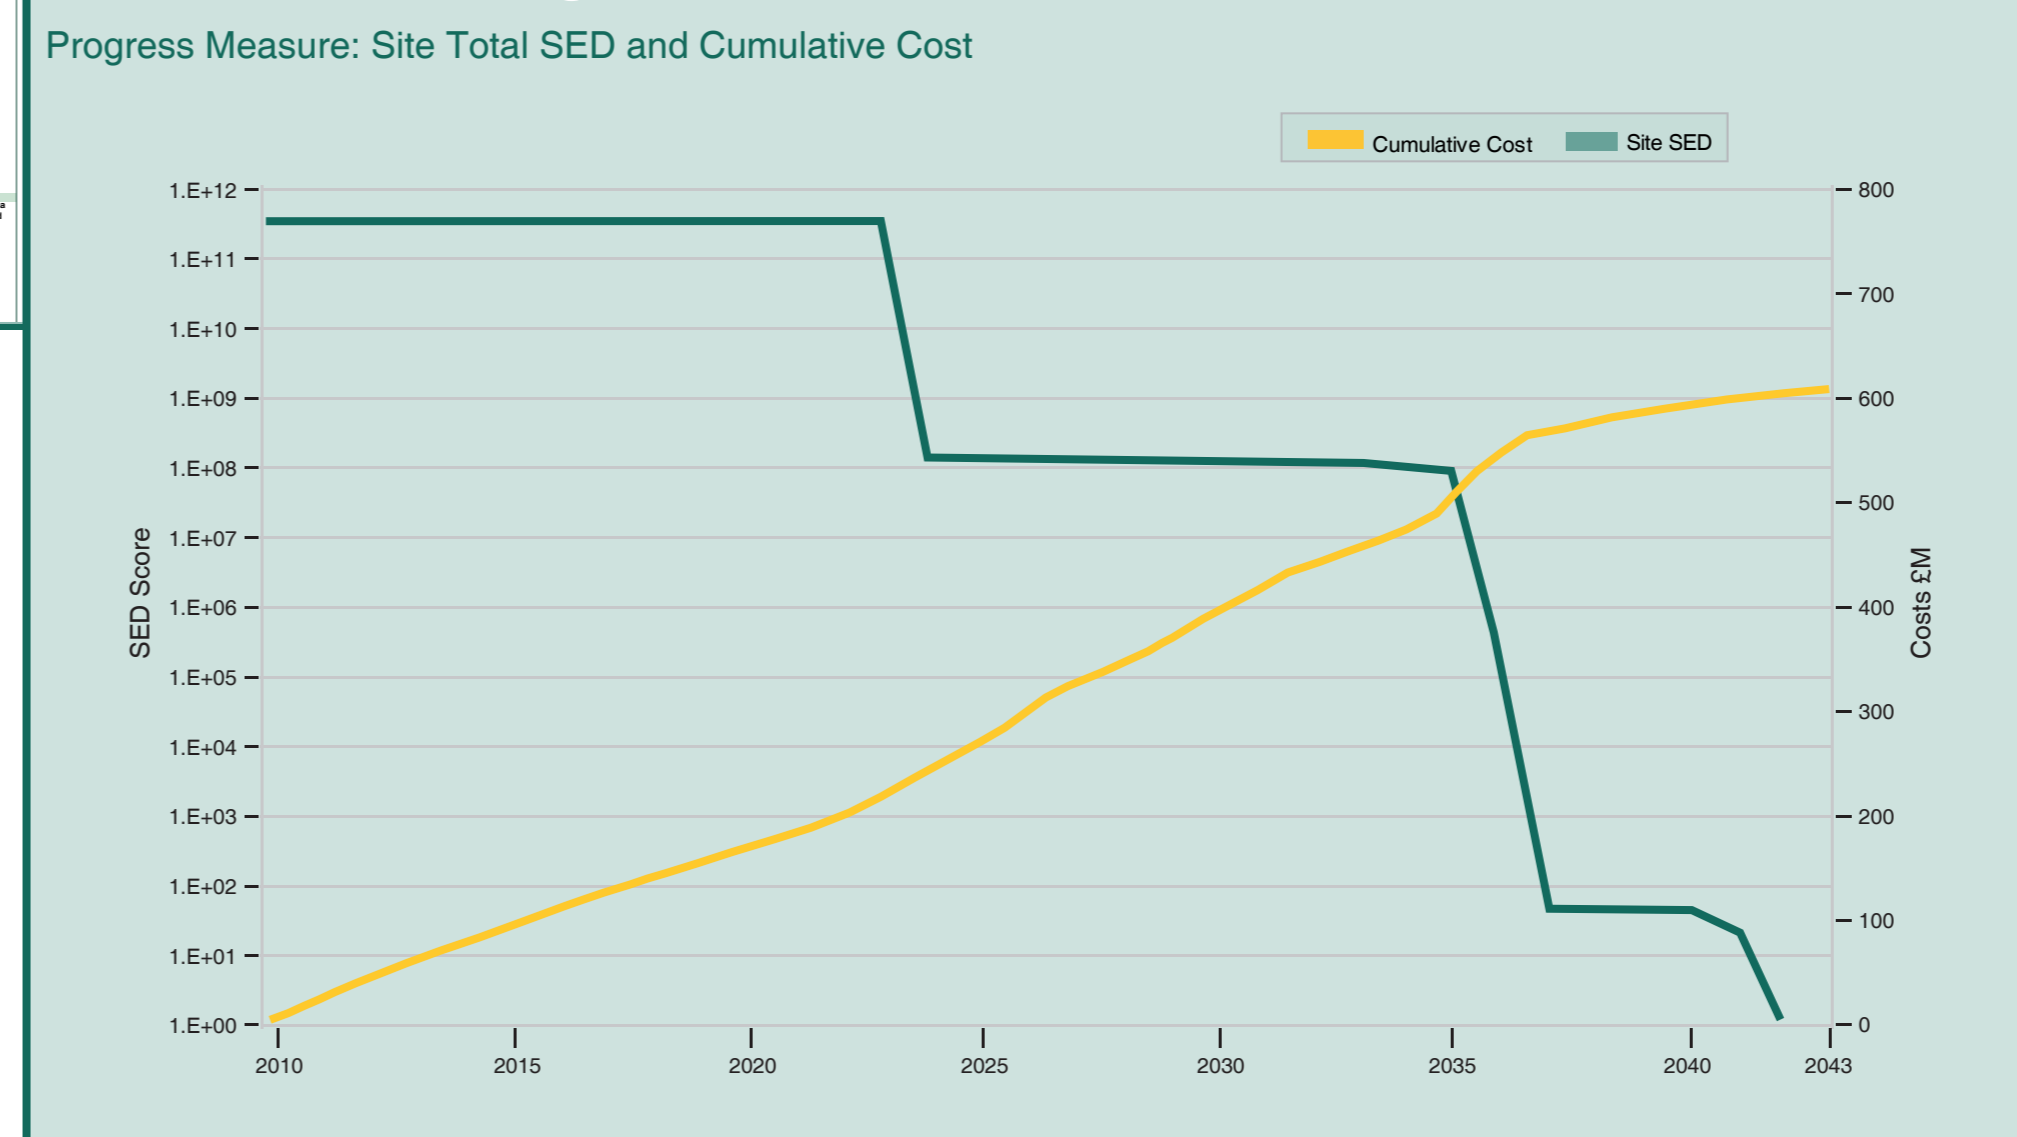

Key Phase Graph

